


SW 14th & Been Intersection

Project Status Update 15MAR23

Project Schedule

Design Notice to Proceed:
27JUL21

30% Plan Submittal: 22OCT21
60% Plan Submittal: MAR23
90% Plan Submittal: JUN23
Final Plan Submittal: JUL23
Begin Construction: DEC23
End Construction: APR24

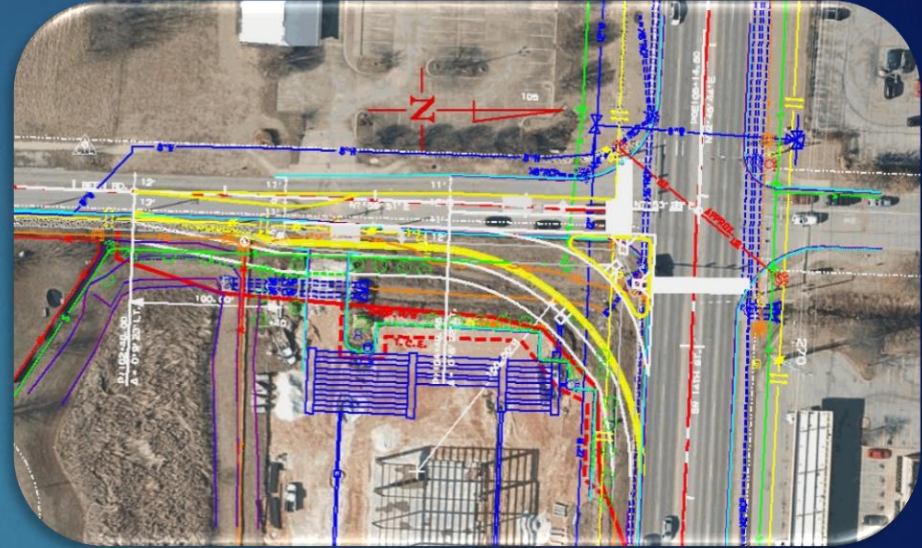

Notes

Hydraulic problems have been solved.

Project Contacts

City of Bentonville: Andrea Jobe, PE
ajobe@bentonvillear.com
Engineer: Jacobs Engineering Group
Contractor: TBD

Action Items

- ☐ Begin the pavement design.
- ☐ Continue with the 60% design
