


SW 7th and C Lateral

Project Status Update 20/JAN/2023

Project Schedule

Design Notice to Proceed: 15/JUL/2021
Begin Survey Work: 27/AUG/2021
Survey Field Work Complete: 10/SEP/2021
50% Design Plans 22/SEP/2021
Public Hearing Held 29/SEP/2021
90% Design Plans 15/OCT/2021
Planned Construction Start Date 15/FEB/2023
Planned Completion Date 30/MAY/2023

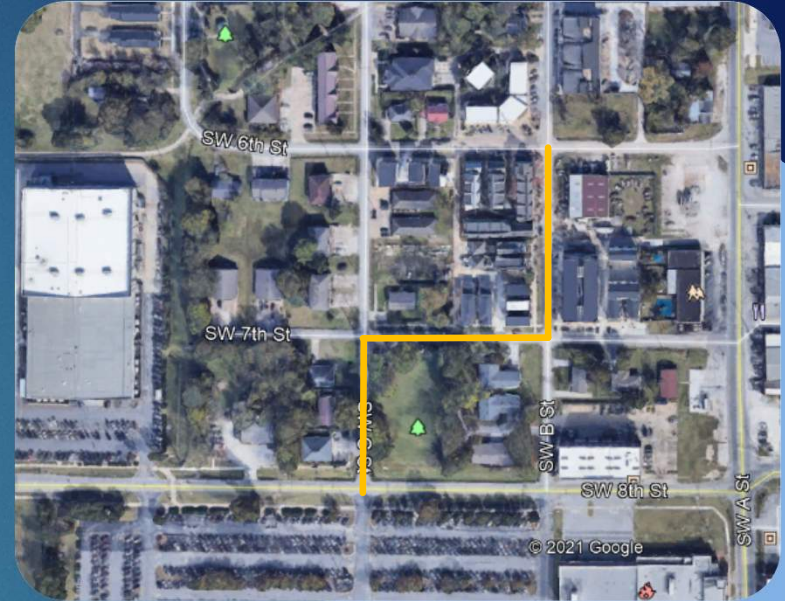

Notes

Project awarded to NEC.

Project Contacts

City of Bentonville: Jarrod Brightwell, PE

jbrightwell@bentonvillear.com

Engineer: Daniel Ellis, PE

Engineer: Luke Jost, PE

Engineer: Libby Topping

Contractor: TBD

Action Items

- Awaiting signed contracts/bonds from Contractor
- ADH Water improvement updates
