

Tiger Blvd Overpass

Project Status Update 16SEP22

Project Schedule

Design Notice to Proceed: 19JUL21

30% Plan Submitted 28Jan22


Revised 30% Submitted 10Mar22

60% Plans TBD

Public Feedback June22

90% Plans 23Sep22

Construction Jul23 - Sept24

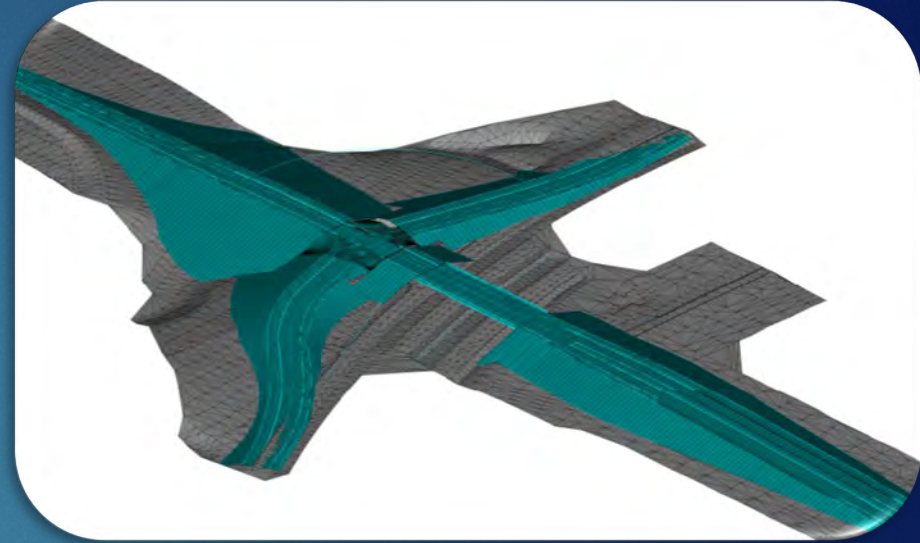

Notes

Wall locations and ROW update from City and property owners. Awaiting comments.

Project Contacts

City of Bentonville: Jarrod Brightwell, PE

jbrightwell@bentonvillear.com

Engineer: Volkert - Ronny Loe, P.E.

Contractor: TBD ronny.loe@volkert.com

Action Items

- Roundabout location east of I49
- Review utility relocation plan from BEUD.
- Review utility relocation from Bentonville Water.
- ARDOT Airspace permit in progress.
