

# Rainbow Curve Improvements

Project Status Update 06MAY22

## Project Schedule

Design Notice to Proceed: 15JUL21

Planning Analysis Submittal: 12DEC21

Alternate Chosen: MAY22

30% Plan Submittal: JUL22

60% Plan Submittal: OCT22


90% Plan Submittal: MAR23

Final Plan Submittal: MAY23

Begin Construction: AUG23

End Construction: JAN25

## Speed Heat Map – 2043 PM

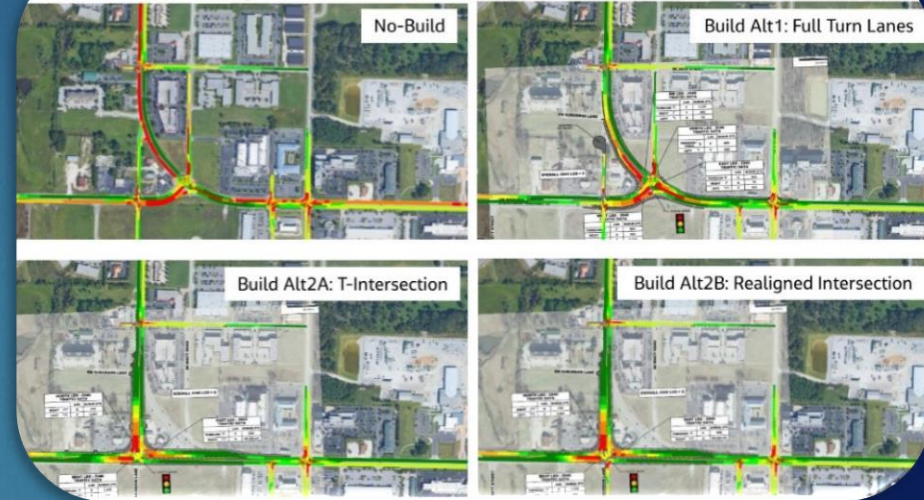

## Notes

Additional information for Alts. 1, 2A, & 2B Submitted 17FEB22

Additional information for Alt. 4 Submitted 25MAR22

## Project Contacts

City of Bentonville: Jarrod Brightwell, PE

[jbrightwell@bentonvillear.com](mailto:jbrightwell@bentonvillear.com)

Engineer: Jacobs Engineering Group

Contractor: TBD

## Action Items

- City to review additional information for Alts. 1, 2A, 2B, & 4.
- Meet with the City to discuss the alternates.
