

Tiger Blvd Overpass

Project Status Update 27JAN23

Project Schedule

Design Notice to Proceed: 19JUL21


30% Plan Submitted 28Jan22

Revised 30% Submitted 10Mar22

60% Plans TBD

90% Plans TBD

Construction Sept23 - Nov24

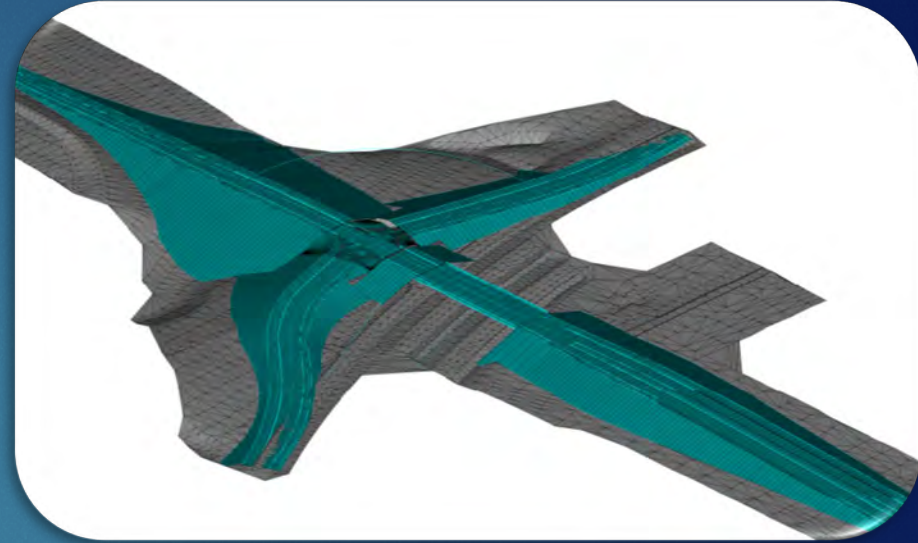

Notes

Roadway model with SW wall location to discuss with property owners. Traffic analysis of roundabouts in process.

Project Contacts

City of Bentonville: Jarrod Brightwell, PE
jbrightwell@bentonvillear.com

Engineer: Volkert - Ronny Loe, PE
ronny.loe@volkert.com

Contractor: TBD

Action Items

- Review utility relocation plan from BEUD.
- Review utility relocation from Bentonville Water.
- ARDOT Airspace permit in progress.
- Check fiber location with Walmart staff
