


Little Osage Trib 2 Phase 2

Project Status Update 13JAN23

Project Schedule

Design N-T-P:	29 JUL21
Original Project Plans:	2015
60% Redesign Plans:	20 JAN22
90% Plans:	04 MAR22
Begin Construction:	TBD
Planned Completion:	TBD

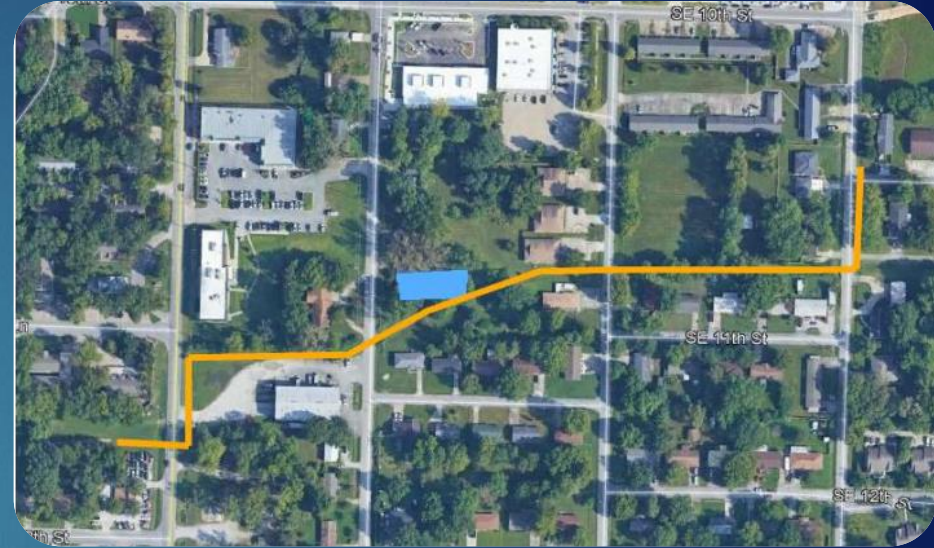

Notes

Project currently on hold due to utility conflicts. Minor redesign of sewer submitted to BWU for review.

Project Contacts

City of Bentonville: Andrea Jobe, P.E.

ajobe@bentonvillear.com

Engineer: Bill Burnett, P.E.

Contractor: TBD

Action Items

- Obtain sign-off from Water Dept
- Investigate remaining franchise utility conflicts
- Obtain STAA & Floodplain Development Permits
- Rebid project
