


SW 14th & Been Intersection

Project Status Update 31 JAN23

Project Schedule

Design Notice to Proceed:
27 JUL21

30% Plan Submittal: 22 OCT21
60% Plan Submittal: JAN23
90% Plan Submittal: MAR23
Final Plan Submittal: MAY23
Begin Construction: OCT23
End Construction: FEB24

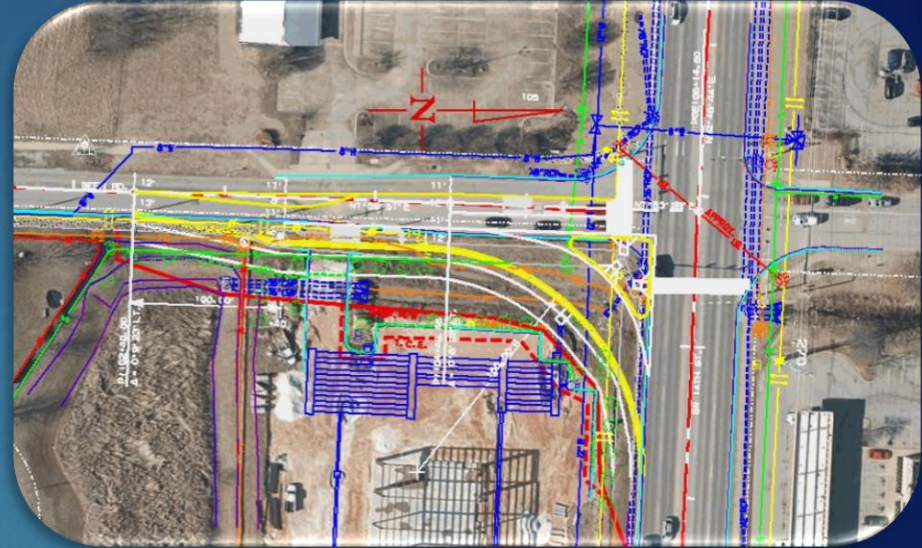

Notes

60% plans delayed due to hydraulics

Project Contacts

City of Bentonville: Andrea Jobe, PE
ajobe@bentonvillear.com
Engineer: Jacobs Engineering Group
Contractor: TBD

Action Items

- Continue with the hydraulic analysis.
 - Design storm water detention
 - Checking with ARDOT about what they will require in this situation.
- Begin the pavement design.
- Continue with the 60% design
