


# SW 7th and C Lateral

Project Status Update 10/MAR/2023

## Project Schedule

Design Notice to Proceed: 15/JUL/2021  
Begin Survey Work: 27/AUG/2021  
Survey Field Work Complete: 10/SEP/2021  
50% Design Plans 22/SEP/2021  
Public Hearing Held 29/SEP/2021  
90% Design Plans 15/OCT/2021  
Planned Construction Start Date 01/APR/2023  
Planned Completion Date 15/JULY/2023

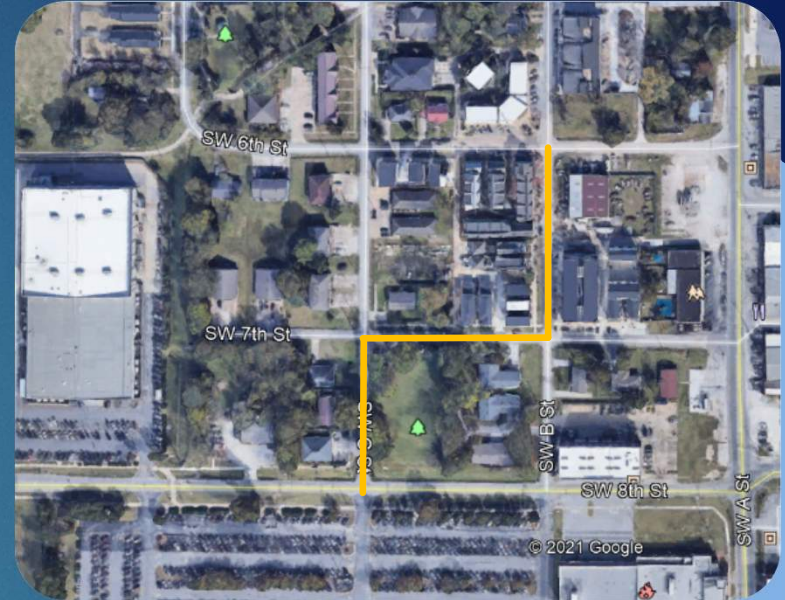

## Notes

Project awarded to NEC.

## Project Contacts

City of Bentonville: Jarrod Brightwell, PE

[jbrightwell@bentonvillear.com](mailto:jbrightwell@bentonvillear.com)

Engineer: Daniel Ellis, PE

Engineer: Luke Jost, PE

Engineer: Libby Topping

Contractor: TBD

## Action Items

- Awaiting ROW Acquisition
- Awaiting ATT Relocation
