

# Rainbow Curve Improvements

Project Status Update 17JUN22

## Project Schedule

Design Notice to Proceed: 15JUL21

Planning Analysis Submittal: 12DEC21

Alternate Chosen: 11MAY22

30% Plan Submittal: JUL22


60% Plan Submittal: OCT22

90% Plan Submittal: APR23

Final Plan Submittal: MAY23

Begin Construction: AUG23

End Construction: JAN25

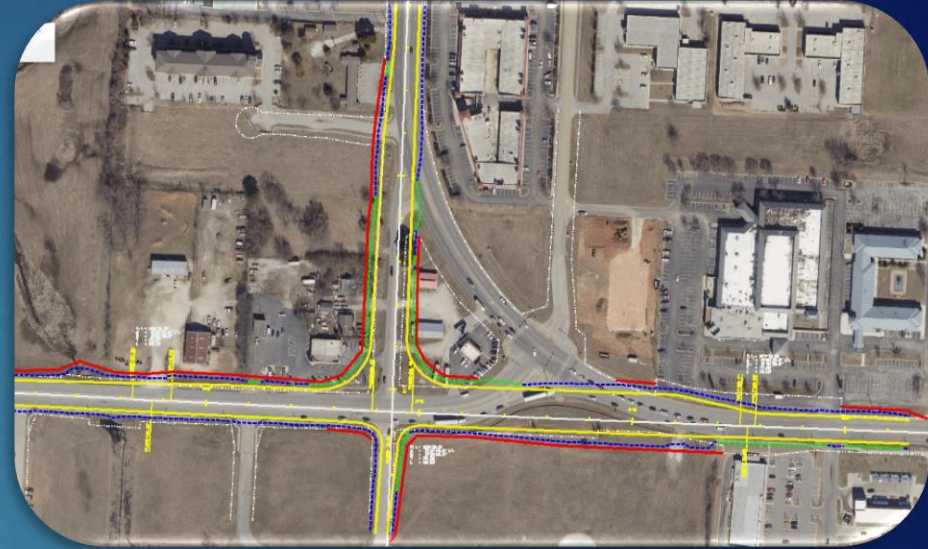

## Notes

Alternate 2B chosen by the City

## Project Contacts

City of Bentonville: Jarrod Brightwell, PE  
jbrightwell@bentonvillear.com

Engineer: Jacobs Engineering Group  
Contractor: TBD

## Action Items

- Continue 30% design of Alternate 2B.
