

# Walton Blvd. & Medical Center Pkwy. Intersection Improvements

## Project Status Update 06MAY2022

### Project Schedule


Design Notice to Proceed: 29 JUL 21

Conceptual Plan Submittal: 11/12/21

Preliminary Plan Submittal: 01/31/22

Final Plan Submittal: 05/16/22

Construction estimated to commence: December 2022 (assuming 6 months for R/W acquisition and utility relocations)

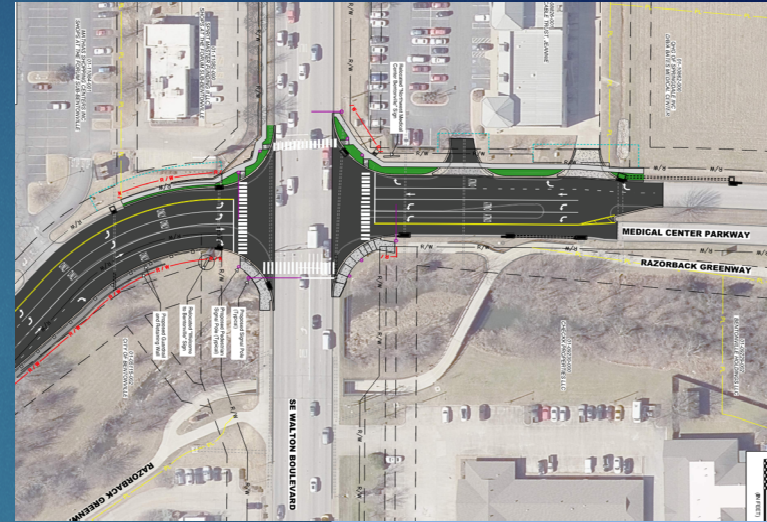

### Notes

- Submitted acquisition documents – May 2nd.
- Performing QA/QC checks on final construction drawings.
- Preparing project specifications.

### Project Contacts

City of Bentonville: Jarrod Brightwell, PE

Email: [jbrightwell@bentonvillear.com](mailto:jbrightwell@bentonvillear.com)

Engineer: Garver

Contractor: TBD

### Action Items

- Submit final construction drawings and specifications – May 16<sup>th</sup>.
- Provide final plans to franchise utilities.
