


# SW I & SW 41<sup>st</sup> Intersection

Project Status Update 27MAY22

## Project Schedule

Design N-T-P:	28JUN21
30% Plans:	24SEP21
Public Feedback:	TBD
60% Plans:	TBD
90% Plans:	TBD
Begin Construction:	TBD
Planned Completion:	TBD

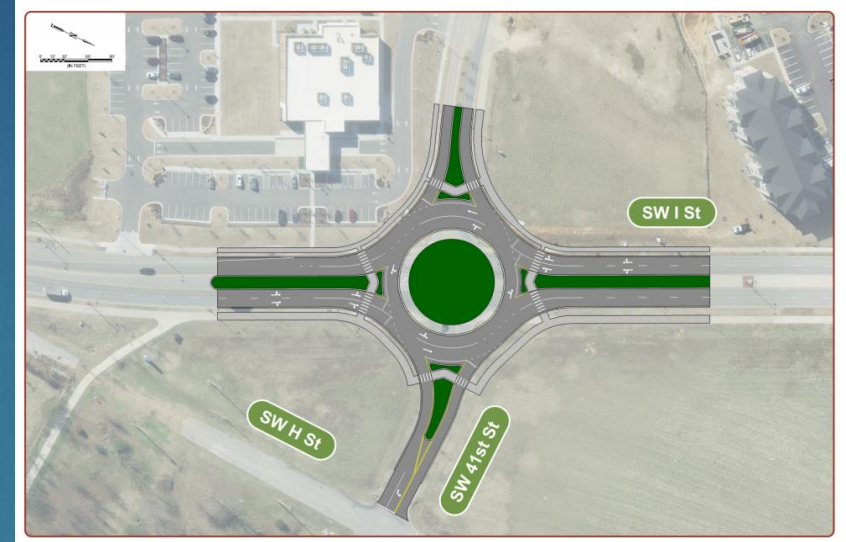

## Notes

30% concept plans submitted.

Project on hold pending outcome of traffic signal warrants analysis.

## Project Contacts

City of Bentonville: Jarrod Brightwell, P.E.

[jbrightwell@bentonvillear.com](mailto:jbrightwell@bentonvillear.com)

Engineer: Bill Burnett, P.E.

Contractor: TBD

## Action Items

- Project now on hold awaiting traffic signal warrants analysis to determine if a signal may be the best alternative for this intersection.
