

SW28th Featherston to SW I

Project Status Update 17MAR23

Project Schedule

Design Notice to Proceed: 19JUL21


30% Plan Submitted 10Jan22

60% Plans Nov22

Public Feedback 22Apr22

100% Plans Feb23

Construction June23 - Aug24

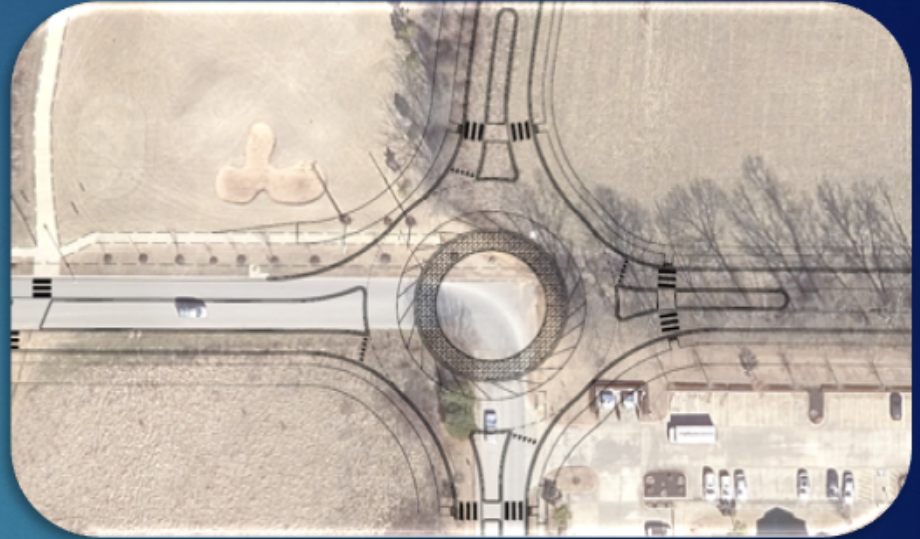

Notes

Bid opening 3/14/2023. Review and recommendation for bid award. ROW acquisition underway.

Project Contacts

City of Bentonville: Andrea Jobe, PE
ajobe@bentonvillear.com
Engineer: Volkert: Reed Hill, P.E.
reed.hill@volkert.com
Contractor: TBD

Action Items

- Wetland clearance process
- Coordinate with BEUD for new lines
- Value determinations for ROW and easements
