


Little Osage Trib 2 Phase 2

Project Status Update 17JUN22

Project Schedule

Design N-T-P:	29 JUL21
Original Project Plans:	2015
60% Redesign Plans:	20 JAN22
90% Plans:	04 MAR22
Begin Construction:	18 JUL22
Planned Completion:	21 JUL23

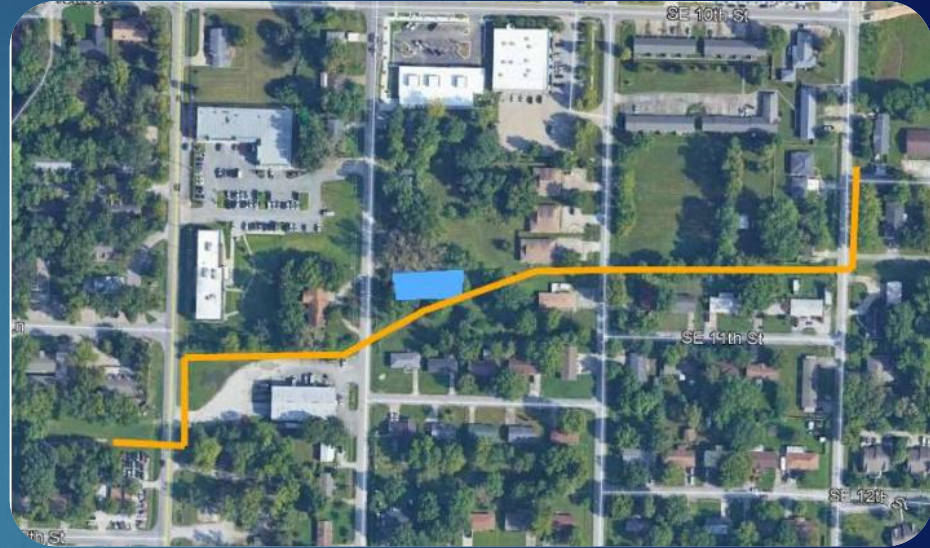

Notes

90% plans submitted for review.

Project Contacts

City of Bentonville: Andrea Jobe, P.E.

ajobe@bentonvillear.com

Engineer: Bill Burnett, P.E.

Contractor: TBD

Action Items

- Awaiting ADH 2nd review / approval.
- Prepare construction contract & specs.
