


Little Osage Trib 2 Phase 2

Project Status Update 06MAY22

Project Schedule

Design N-T-P:	29JUL21
Original Project Plans:	2015
60% Redesign Plans:	20JAN22
90% Plans:	04MAR22
Begin Construction:	13JUN22
Planned Completion:	16JUN23

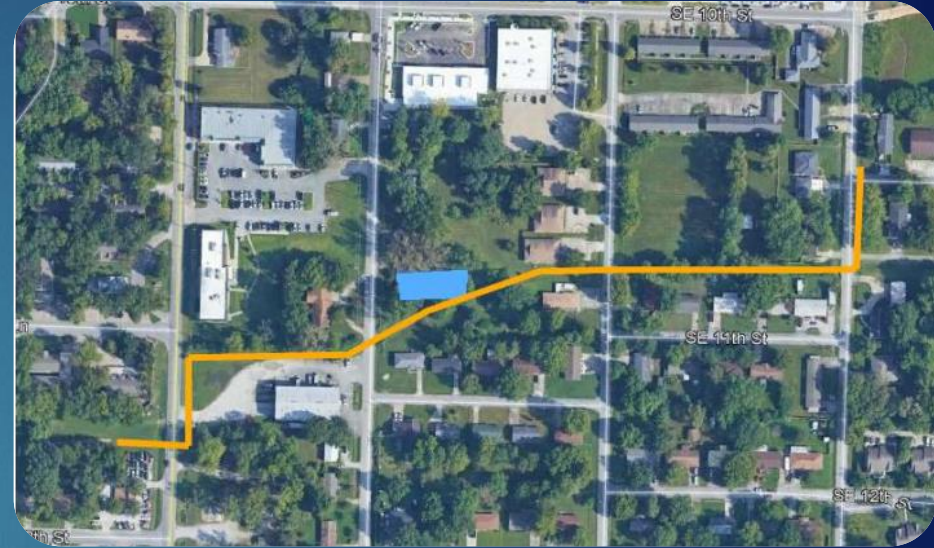

Notes

90% plans submitted for review.

Project Contacts

City of Bentonville: Andrea Jobe, P.E.

ajobe@bentonvillear.com

Engineer: Bill Burnett, P.E.

Contractor: TBD

Action Items

- Submit to ADH for review.
