


# SW 14<sup>th</sup> & Been Intersection

Project Status Update 18NOV22

## Project Schedule

Design Notice to Proceed:  
27JUL21

30% Plan Submittal: 22OCT21  
60% Plan Submittal: NOV22  
90% Plan Submittal: JAN23  
Final Plan Submittal: FEB23  
Begin Construction: JUL23  
End Construction: NOV23

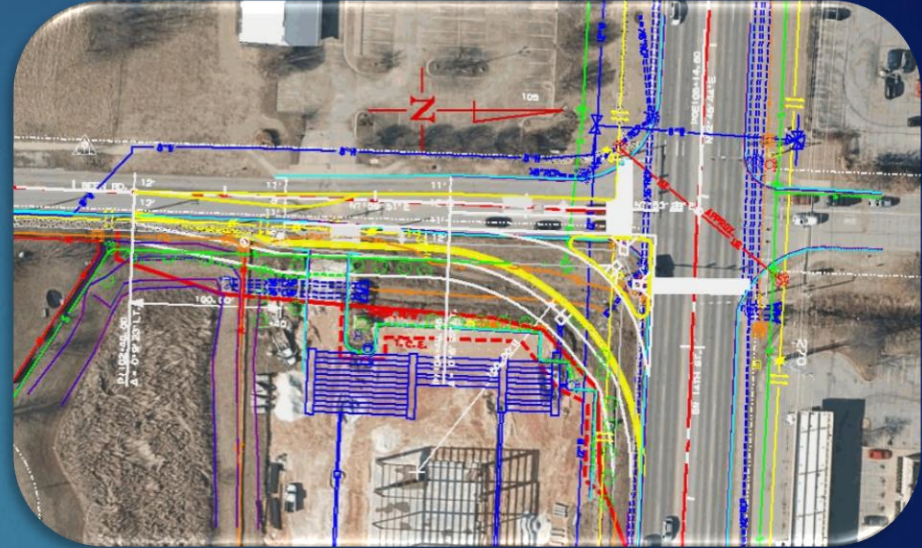

## Notes

Additional Survey Completed

## Project Contacts

City of Bentonville: Andrea Jobe, PE  
ajobe@bentonvillear.com  
Engineer: Jacobs Engineering Group  
Contractor: TBD

## Action Items

- Continue with the hydraulic analysis.
- Begin the pavement design.
- Proceed with the 60% design with the following answers received from the City:
  - Construct shared use path (not sidewalk)
  - Adjust the green space between the shared use path and curb to avoid the new bank parking lot
  - Adjust the grading to replace the existing open ditch with storm sewer
