


# SW 14<sup>th</sup> & Been Intersection

Project Status Update 08MAR23

## Project Schedule

Design Notice to Proceed:  
27JUL21

30% Plan Submittal: 22OCT21  
60% Plan Submittal: MAR23  
90% Plan Submittal: JUN23  
Final Plan Submittal: JUL23  
Begin Construction: DEC23  
End Construction: APR24

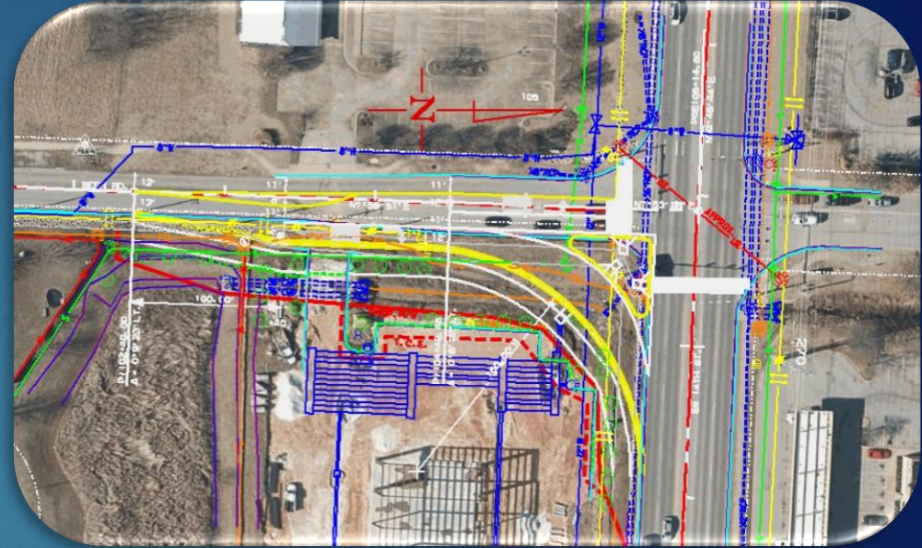

## Notes

Hydraulic problems have been solved.

## Project Contacts

City of Bentonville: Andrea Jobe, PE  
ajobe@bentonvillear.com  
Engineer: Jacobs Engineering Group  
Contractor: TBD

## Action Items

- Begin the pavement design.
- Continue with the 60% design
