

Walton Blvd. & SE J Street Intersection Improvements

Project Status Update 17JUNE2022

Project Schedule


Design Notice to Proceed: 29JUL21

Conceptual Plan Submittal: 11/12/21

Preliminary Plan Submittal: 01/31/22

Final Plan Submittal: 05/16/2022

Construction estimated to commence: December 2022 (assuming six months for R/W acquisition and utility relocations)

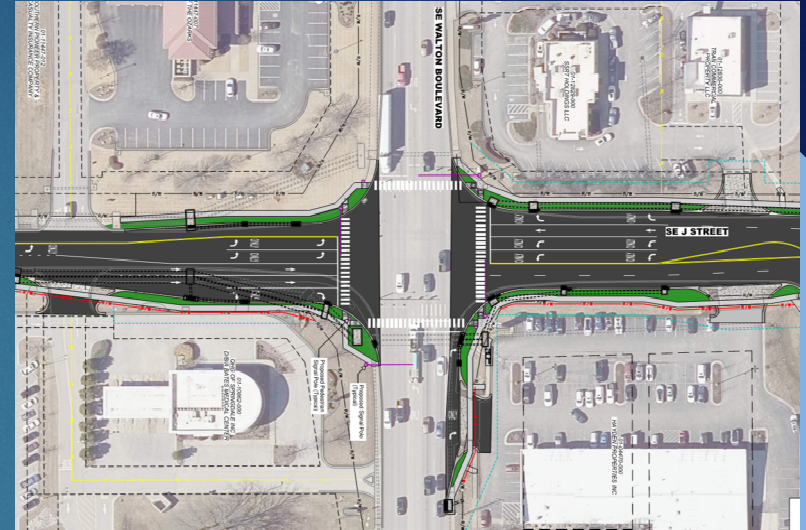

Notes

- Received final review comments from Engineering – May 24th.
- Received final review comments from BEUD and BUD on 6/15/22
- Submitted final plans to Franchise Utilities.

Project Contacts

City of Bentonville: Jarrod Brightwell, PE

Email: jbrightwell@bentonvillear.com

Engineer: Garver

Contractor: TBD

Action Items

- ☐ Address City Comments.
- ☐ In-person inter-department meeting scheduled for June 28th.
- ☐ Submit final plans to ARDOT for construction permit.
