


SW 14th & Been Intersection

Project Status Update 29 JUL22

Project Schedule

Design Notice to Proceed:
27 JUL21

30% Plan Submittal: 22 OCT21
60% Plan Submittal: AUG22
90% Plan Submittal: OCT22
Final Plan Submittal: DEC22
Begin Construction: MAR23
End Construction: JUL23

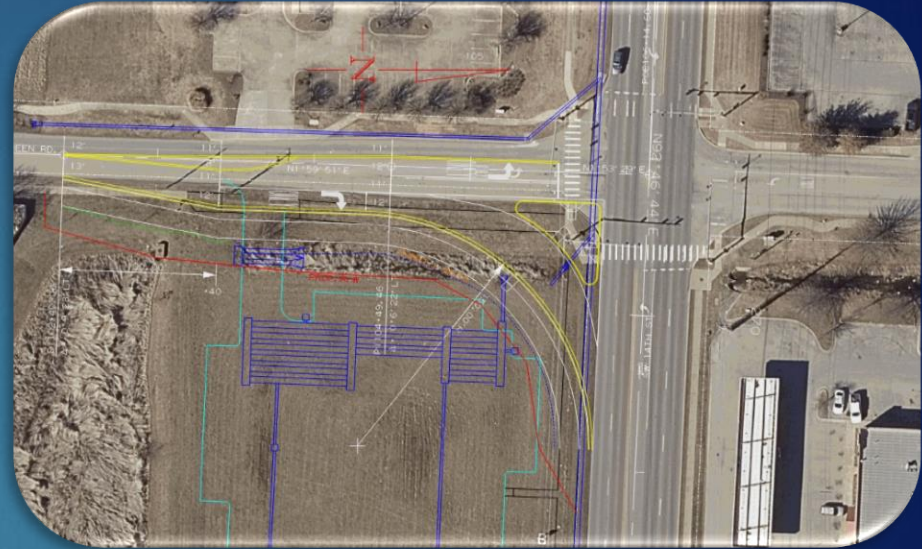

Notes

Meeting with City held 18 JUL22

Project Contacts

City of Bentonville: Andrea Jobe, PE
ajobe@bentonvillear.com
Engineer: Jacobs Engineering Group
Contractor: TBD

Action Items

- Continue with the hydraulic analysis.
- Begin the pavement design.
- Proceed with the 60% design with the following answers received from the City:
 - Construct shared use path (not sidewalk)
 - Adjust the green space between the shared use path and curb to avoid the new bank parking lot
 - Adjust the grading to replace the existing open ditch with storm sewer
