


North 8th and Main

Project Status Update 18/NOV/2022

Project Schedule

Design Notice to Proceed: 15/JUL/2021
Begin Survey Work: 30/JUL/2021
Survey Field Work Complete: 16/AUG/2021
Survey Work Complete: 13/SEP/2021
50% Design Plans 22/SEP/2021
Public Hearing Held 29/SEP/2021
90% Design Plans 23/DEC/2021
Planned Const. Start Date 15/JAN/2023
Planned Completion Date 15/JUL/2023

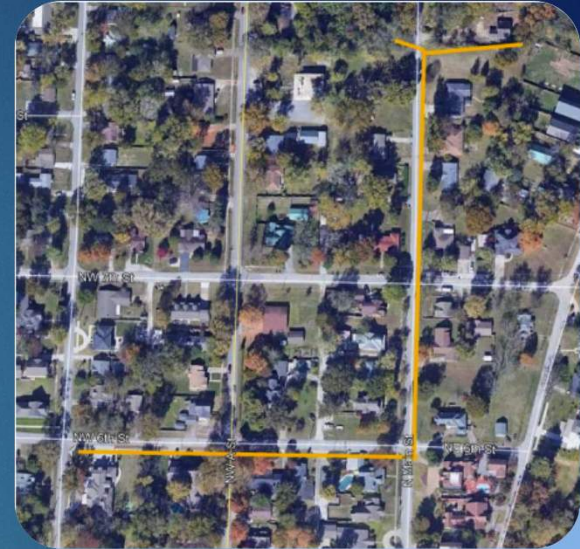

Notes On Hold.

Project Contacts

City of Bentonville: Andrea Jobe, PE
ajobe@bentonvillear.com
Engineer: Daniel Ellis, PE
Engineer: Luke Jost, PE
Engineer: Libby Topping
Contractor:

Action Items

- Revised plans submitted 15/JULY/2022
- Schedule ATA Meeting
- Preparation of Right-of-Way Procurement Documents (after CoB buy-in of ROW shown on plans)
- Utility Coordination ongoing
