


S Walton & SW 5th Intersection

Project Status Update 29JUL22

Project Schedule

Design Notice to Proceed:
23JUL21

30% Plan Submittal: 22OCT21
60% Plan Submittal: 02JUN22
90% Plan Submittal: SEP22
Final Plan Submittal: NOV22
Begin Construction: FEB23
End Construction: JUN23

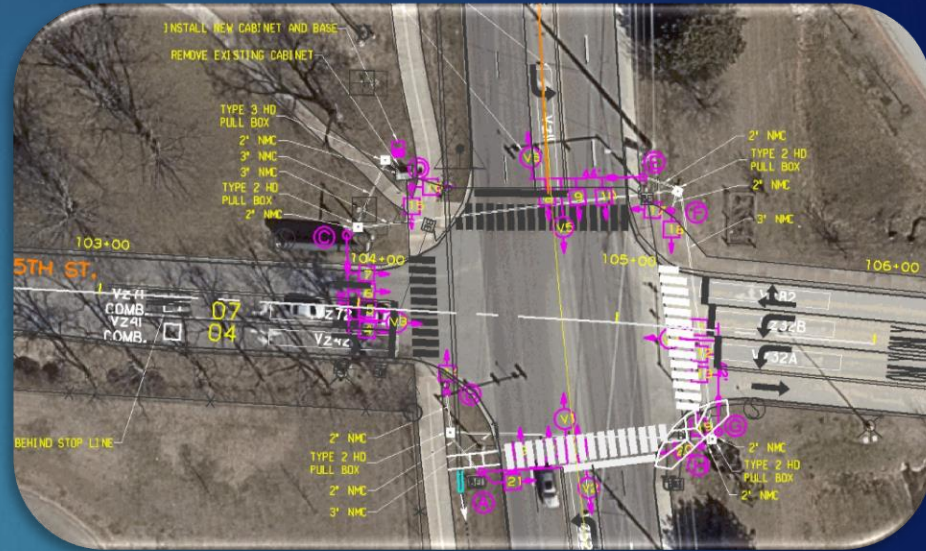

Notes

Meeting with City held 18JUL22

Project Contacts

City of Bentonville: Andrea Jobe, PE
ajobe@bentonvillear.com
Engineer: Jacobs Engineering Group
Contractor: TBD

Action Items

- Revise 60% plans and resubmit
