

SW28th Featherston to SW I

Project Status Update 29 JUL22

Project Schedule

Design Notice to Proceed: 19JUL21


30% Plan Submitted 10Jan22

60% Plans Revising Schedule

Public Feedback 22Apr22

90% Plans Revising Schedule

Construction May23 - May24

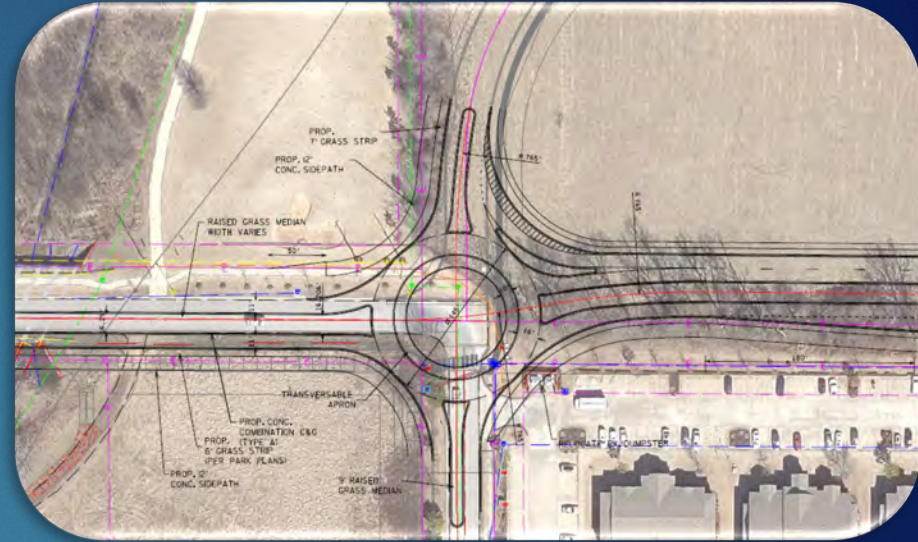

Notes

Drainage box/spread awaiting City concurrence. Line and grade given to BEUD for preliminary layouts.

Project Contacts

City of Bentonville: Andrea Jobe, PE
ajobe@bentonvillear.com

Engineer: Volkert: Reed Hill, P.E.
reed.hill@volkert.com

Contractor: TBD

Action Items

- Geotechnical evaluation by GHBW access.
- Review utilities with BEUD and Bentonville Water and Sewer.
- Redesign drainage
- Revise project schedule
- Update construction estimate
