


# North 8<sup>th</sup> and Main

Project Status Update 17/JUNE/2022

## Project Schedule

Design Notice to Proceed: 15/JUL/2021  
Begin Survey Work: 30/JUL/2021  
Survey Field Work Complete: 16/AUG/2021  
Survey Work Complete: 13/SEP/2021  
50% Design Plans 22/SEP/2021  
Public Hearing Held 29/SEP/2021  
90% Design Plans 23/DEC/2021  
Planned Const. Start Date 02/SEP/2022  
Planned Completion Date 01/APR/2023

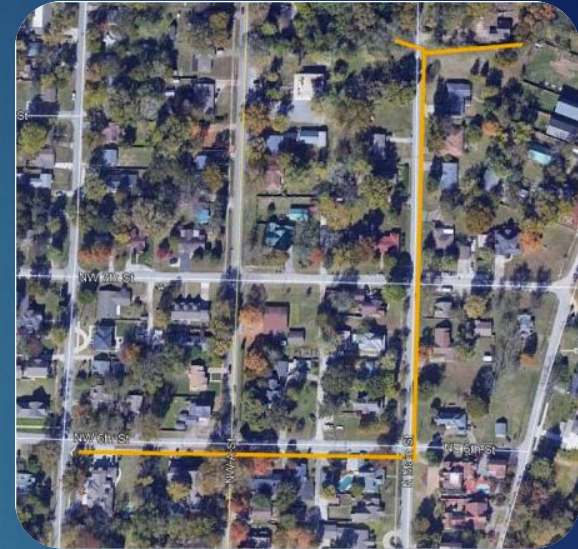

## Notes

Revise Plans to avoid Main Street  
Overhead Electric lines.

## Project Contacts

City of Bentonville: Andrea Jobe, PE

[ajobe@bentonvillear.com](mailto:ajobe@bentonvillear.com)

Engineer: Daniel Ellis, PE

Engineer: Luke Jost, PE

Engineer: Libby Topping

Contractor:

## Action Items

- Meeting with BEUD & City held. To revise plans to avoid OHE along Main Street. Plans expected June 30.
- Schedule ATA Meeting
- Preparation of Right-of-Way Procurement Documents (after CoB buy-in of ROW shown on plans)
- Utility Coordination ongoing
