

Tiger Blvd Overpass

Project Status Update 18NOV22

Project Schedule

Design Notice to Proceed: 19JUL21

30% Plan Submitted 28Jan22


Revised 30% Submitted 10Mar22

60% Plans Feb23

Public Feedback June22

90% Plans Apr23

Construction Sept23 - Nov24

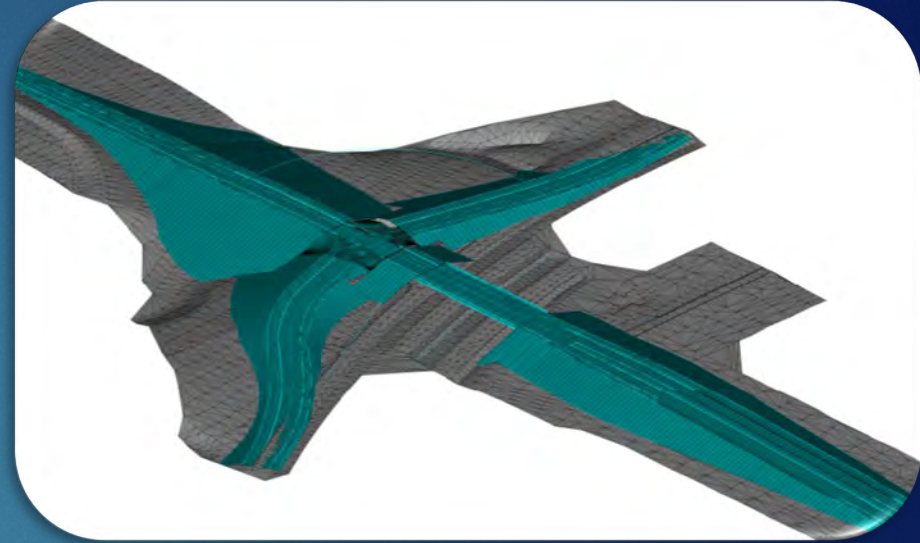

Notes

ROW train submitted west for properties.
Roundabout east side of I-49 being incorporated into roadway.

Project Contacts

City of Bentonville: Jarrod Brightwell, PE

jbrightwell@bentonvillear.com

Engineer: Volkert - Ronny Loe, P.E.

Contractor: TBD

ronny.loe@volkert.com

Action Items

- Review utility relocation plan from BEUD.
- Review utility relocation from Bentonville Water.
- ARDOT Airspace permit in progress.
