


North 8th and Main

Project Status Update 06/MAY/2022

Project Schedule

Design Notice to Proceed: 15/JUL/2021
Begin Survey Work: 30/JUL/2021
Survey Field Work Complete: 16/AUG/2021
Survey Work Complete: 13/SEP/2021
50% Design Plans 22/SEP/2021
Public Hearing Held 29/SEP/2021
90% Design Plans 23/DEC/2021
Planned Const. Start Date 02/SEP/2022
Planned Completion Date 01/APR/2023

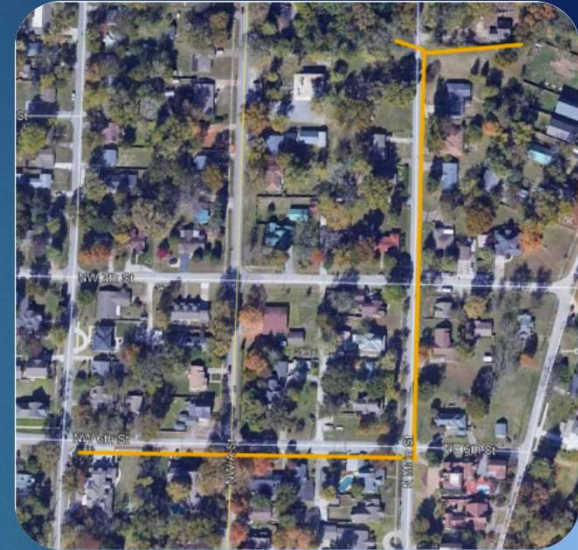

Notes

Submitted revised 90% plans
28/DEC/2021.

Project Contacts

City of Bentonville: Andrea Jobe, PE

ajobe@bentonvillear.com

Engineer: Daniel Ellis, PE

Engineer: Luke Jost, PE

Engineer: Libby Topping

Contractor:

Action Items

- Awaiting on Revised 90% Comments
- Awaiting City input on BEUD conflict
- Schedule ATA Meeting
- Preparation of Right-of-Way Procurement Documents (after CoB buy-in of ROW shown on plans)
- Utility Coordination ongoing
