


Little Osage Trib 2 Phase 2

Project Status Update 18NOV22

Project Schedule

Design N-T-P:	29JUL21
Original Project Plans:	2015
60% Redesign Plans:	20JAN22
90% Plans:	04MAR22
Begin Construction:	TBD
Planned Completion:	TBD

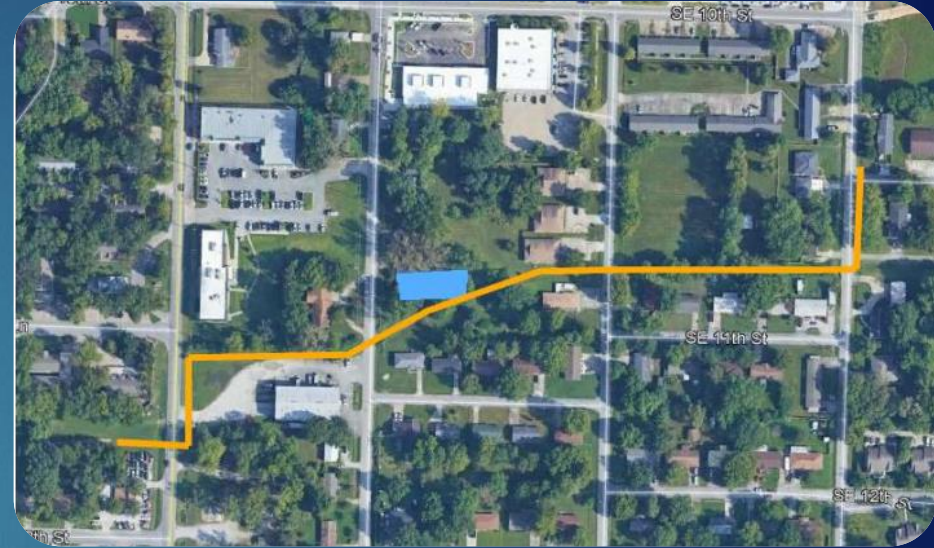

Notes

Project currently on hold due to utility conflicts.

Project Contacts

City of Bentonville: Andrea Jobe, P.E.

ajobe@bentonvillear.com

Engineer: Bill Burnett, P.E.

Contractor: Crow Group

Action Items

- Investigate extent of franchise utility conflicts
- Redesign if required by utility findings
- Rebid project
- Obtain sign-off from Water Dept
- Obtain STAA & Floodplain Development Permits
