


SW 7th and C Lateral

Project Status Update 16/SEPT/2022

Project Schedule

Design Notice to Proceed: 15/JUL/2021
Begin Survey Work: 27/AUG/2021
Survey Field Work Complete: 10/SEP/2021
50% Design Plans 22/SEP/2021
Public Hearing Held 29/SEP/2021
90% Design Plans 15/OCT/2021
Planned Construction Start Date 20/AUG/2022
Planned Completion Date 04/MAR/2023

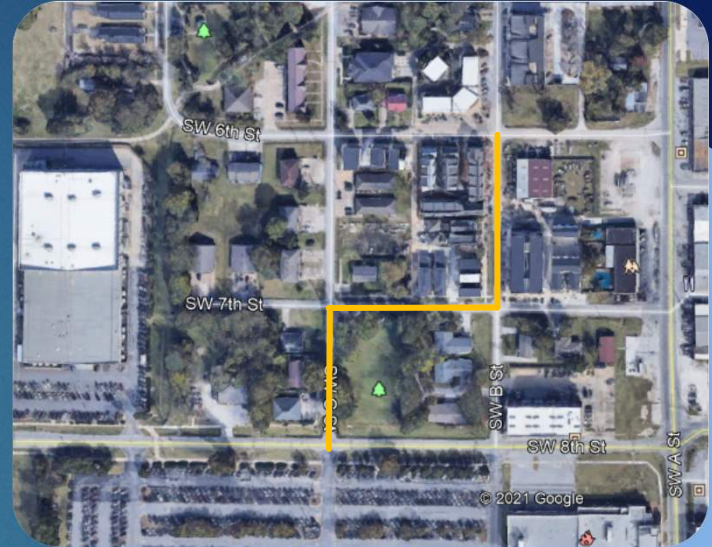

Notes

Bids Received 8/29.

Project Contacts

City of Bentonville: Jarrod Brightwell, PE
jbrightwell@bentonvillear.com
Engineer: Daniel Ellis, PE
Engineer: Luke Jost, PE
Engineer: Libby Topping
Contractor: TBD

Action Items

- Working through ROW/ESMT acquisition
- Award Project to contractor
