

NW 9th and D

Project Status Update 09/17/2021

Project Schedule

Design Notice to Proceed:
06/28/2022


60% Design Submittal: 11/05/2021
100% Design Submittal: 12/31/2021

Notes

CEI met with City on
Monday, August 30th to
discuss 30% comments.

Project Contacts

City of Bentonville: Bryan Wick
Engineer: CEI, Anna Negrete
Contractor: N/A

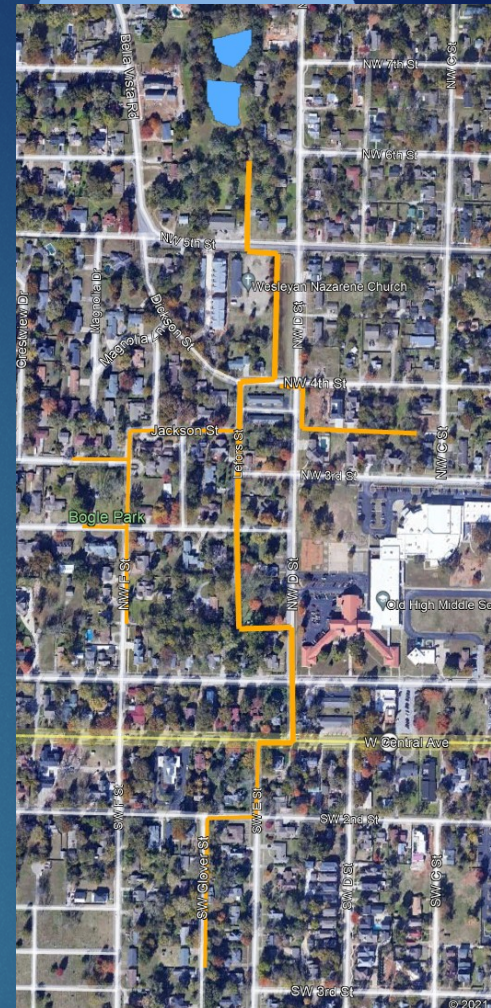

Action Items

- ☐ CEI proceeding with 60% design.
- ☐ Anticipate to beat 60% design submittal date and submit within the next 4-6 weeks.
