


# S Walton & SW 5<sup>th</sup> Intersection

Project Status Update 16SEP22

## Project Schedule

Design Notice to Proceed:  
23JUL21

30% Plan Submittal: 22OCT21  
60% Plan Submittal: 02JUN22  
90% Plan Submittal: SEP22  
Final Plan Submittal: NOV22  
Begin Construction: FEB23  
End Construction: JUN23

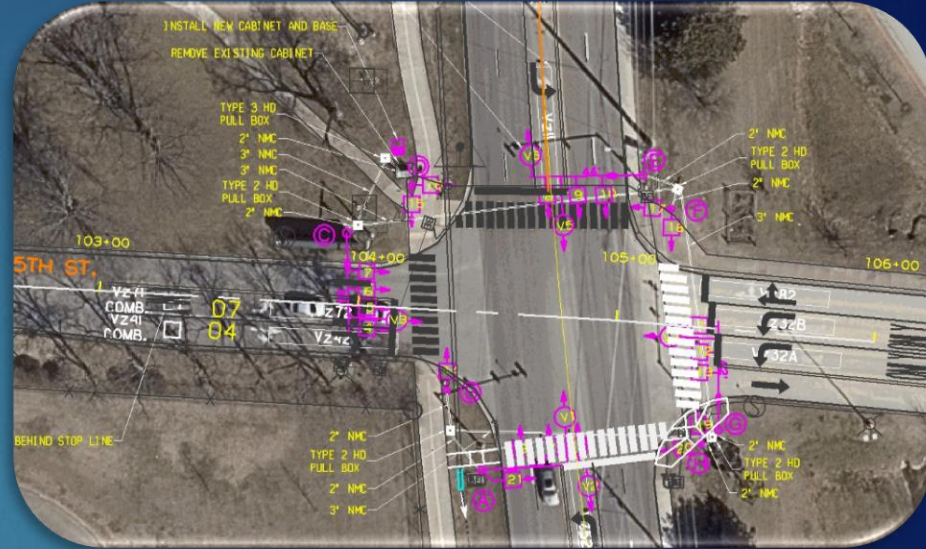

## Notes

Submitted Revised 60% Plans  
13SEP22

## Project Contacts

City of Bentonville: Andrea Jobe, PE  
ajobe@bentonvillear.com  
Engineer: Jacobs Engineering Group  
Contractor: TBD

## Action Items

- City to review revised 60% plans.
