


# NW Tiger & G

Project Status Update 16Sep22

## Project Schedule

Design Notice to Proceed:  
22JUL2021

Final design scheduled for 10/10.  
Construction expected to begin spring 2023, with  
completion expected fall 2023, to coincide with  
summer break.

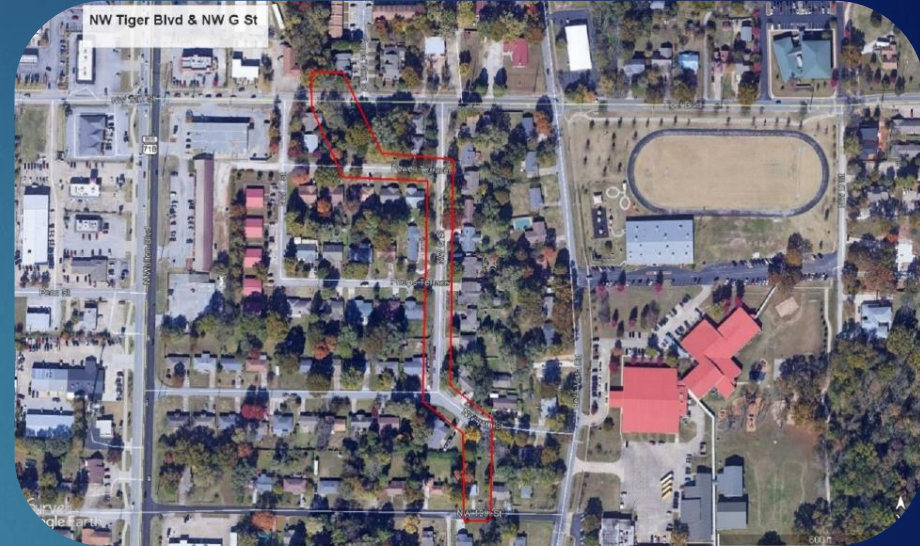

## Notes

### Project Contacts

City of Bentonville: Andrea Jobe, PE  
[ajobe@bentonvillear.com](mailto:ajobe@bentonvillear.com)  
Engineer: Aaron Boll, PE  
Contractor: NA

## Action Items

- ROW appraisals completed
- Utility coordination
- Final design
