

SW28th Featherston to SW I

Project Status Update 05MAY22

Project Schedule

Design Notice to Proceed:
19JUL21


30% Plan Submitted 10Jan22

60% Plans 29April22

Public Feedback 22Apr22

90% Plans 08Jul22

Construction May23 - May24

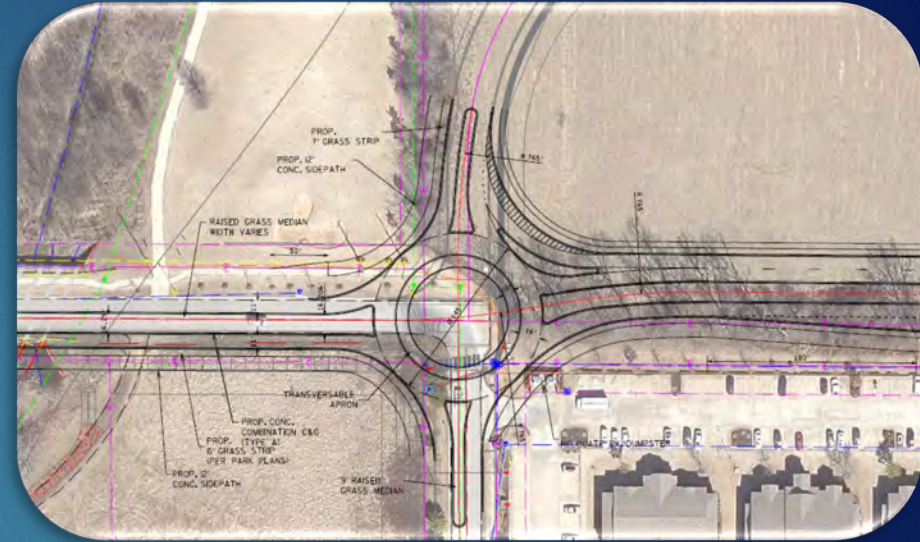

Notes

SW I Intersection modifications due to water concerns. DWG files sent to water, sewer, and BEUD. 60% submittal pending comments.

Project Contacts

City of Bentonville: Andrea Jobe, PE
ajobe@bentonvillear.com

Engineer: Volkert:- Reed Hill, P.E.

reed.hill@volkert.com

Contractor: TBD

Action Items

- Geotechnical evaluation by GHBW.
- Review utilities with BEUD and Bentonville Water and Sewer.
- Existing drainage questions to resolve
