


S Walton & SW 5th Intersection

Project Status Update 18NOV22

Project Schedule

Design Notice to Proceed:
23JUL21

30% Plan Submittal: 22OCT21
60% Plan Submittal: 02JUN22
90% Plan Submittal: NOV22
Final Plan Submittal: JAN23
Begin Construction: APR23
End Construction: AUG23

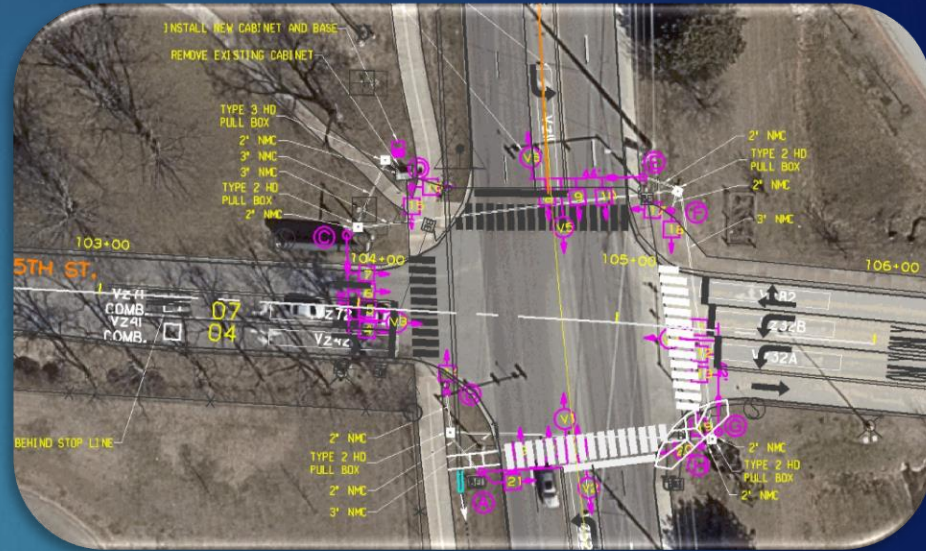

Notes

Received City's Comments on
Rev. 60% Plans 04NOV22

Project Contacts

City of Bentonville: Andrea Jobe, PE
ajobe@bentonvillear.com
Engineer: Jacobs Engineering Group
Contractor: TBD

Action Items

- Address City's Comments and resubmit revised 60% plans
