


S Walton & SW 5th Intersection

Project Status Update 17JUN22

Project Schedule

Design Notice to Proceed:
23JUL21

30% Plan Submittal: 22OCT21
60% Plan Submittal: 02JUN22
90% Plan Submittal: AUG22
Final Plan Submittal: SEP22
Begin Construction: DEC22
End Construction: APR23

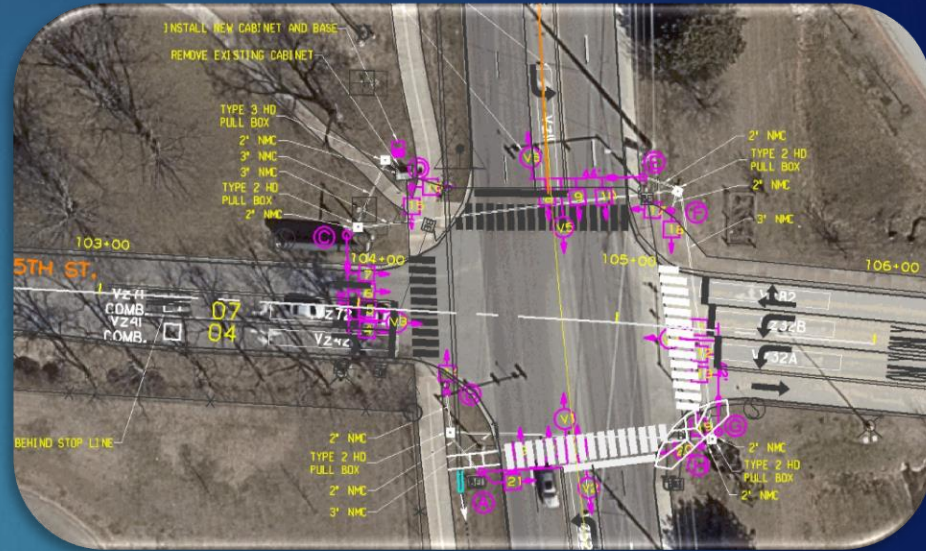

Notes

60% Plans Submitted for Review

Project Contacts

City of Bentonville: Andrea Jobe, PE
ajobe@bentonvillear.com
Engineer: Jacobs Engineering Group
Contractor: TBD

Action Items

- City to review 60% Submittal.
- Complete the 60% OPC.
