


SW I & SW 41st Intersection

Project Status Update 06MAY22

Project Schedule

Design N-T-P:	28JUN21
30% Plans:	24SEP21
Public Feedback:	TBD
60% Plans:	TBD
90% Plans:	TBD
Begin Construction:	TBD
Planned Completion:	TBD

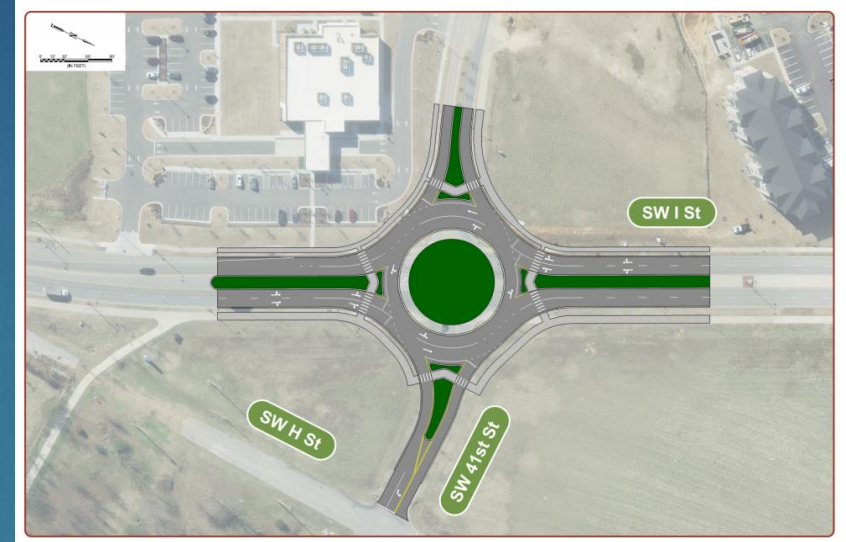

Notes

30% concept plans submitted.

Project on hold pending outcome of traffic signal warrants analysis.

Project Contacts

City of Bentonville: Jarrod Brightwell, P.E.

jbrightwell@bentonvillear.com

Engineer: Bill Burnett, P.E.

Contractor: TBD

Action Items

- Awaiting response from ARDOT regarding the football shaped roundabout previously submitted as "Concept 4" to determine its feasibility.
- Project now on hold as the City collects traffic counts and conducts a traffic signal warrants analysis to determine if a signal may be the best alternative for this intersection.
