


NW Trails End & C

Project Status Update 29 Jul 22

Project Schedule

Design Notice to Proceed:
22 JUL 2021

Final design scheduled to be submitted 8/8.
Construction expected to begin fall 2022, with
completion expected by end of year.

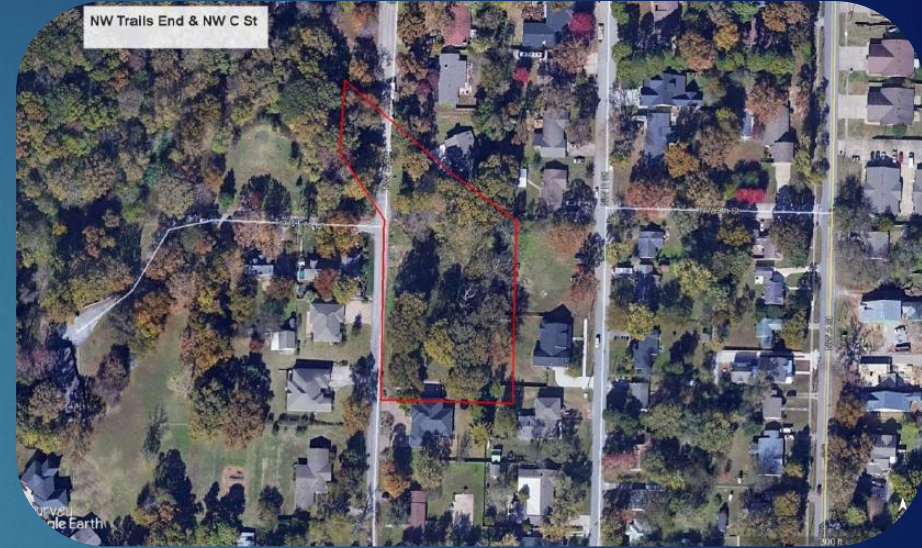

Notes

Project Contacts

City of Bentonville: Andrea Jobe, PE
ajobe@bentonvillear.com
Engineer: Aaron Boll, PE
Contractor: NA

Action Items

- ROW appraisal underway, expected to be completed by end of August
- Utility coordination
