


SW 14th & Been Intersection

Project Status Update 15SEP23

Project Schedule

90% Plan Submittal: NOV23
Final Plan Submittal: DEC23
Project Bid: Reviewing Funding

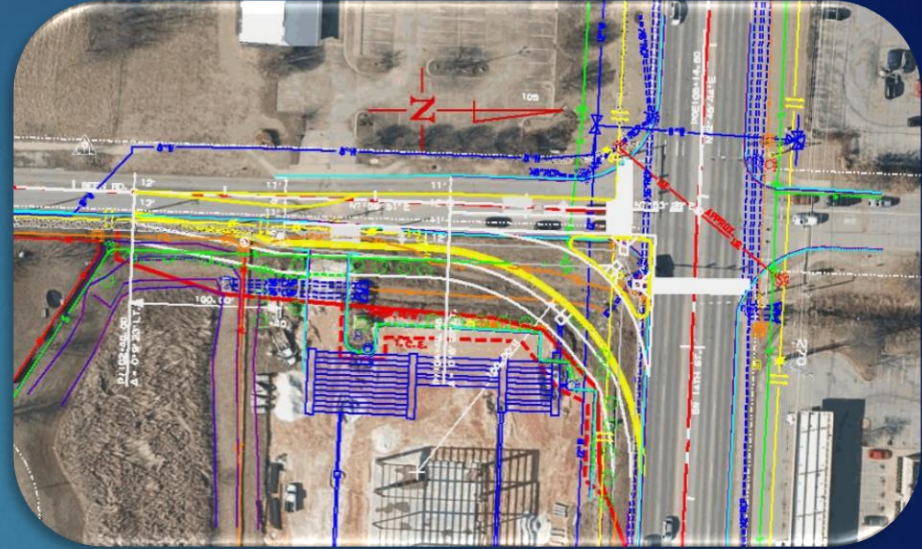

Notes

60% Plans submitted 28JUL23

Project Contacts

City of Bentonville: Cody Vaughn, EI
cvaughn@bentonvillear.com
Engineer: Jacobs Engineering Group
Contractor: TBD

Action Items

- Begin the pavement design.
- City to review 60% plans.
