


S Walton & SW 5th Intersection

Project Status Update 08MAR23

Project Schedule

Design Notice to Proceed:
23JUL21

30% Plan Submittal: 22OCT21
60% Plan Submittal: 02JUN22
Final Plan Submittal: 27JAN23
Letting Date: 02MAR23
Begin Construction: JUL23
End Construction: NOV23

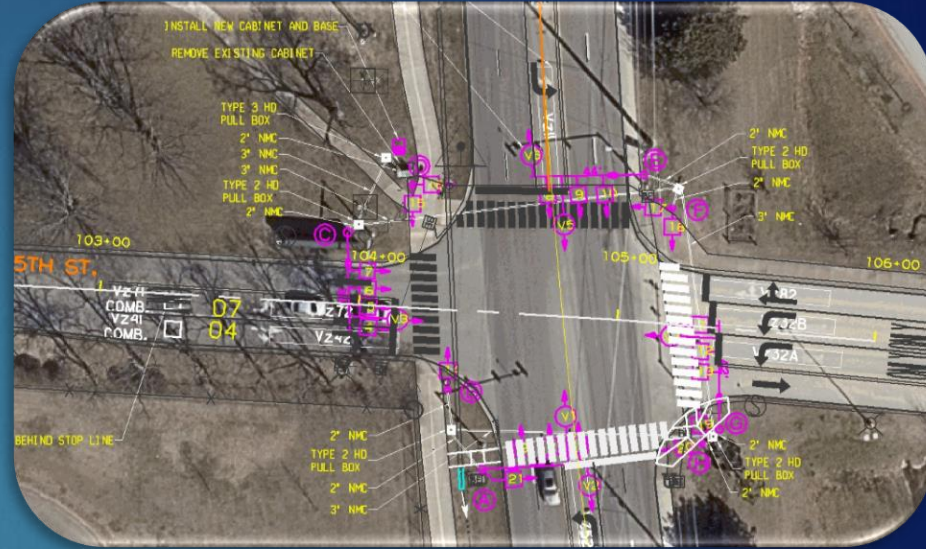

Notes

Letting Held-1 Bid Received
Bid Analysis & Recommendation
sent to City

Project Contacts

City of Bentonville: Andrea Jobe, PE
ajobe@bentonvillear.com
Engineer: Jacobs Engineering Group
Contractor: TBD

Action Items

- City to determine if the bid will be accepted or rejected.
