

SW28th Featherston to SW I

Project Status Update 17JUN22

Project Schedule

Design Notice to Proceed: 19JUL21


30% Plan Submitted 10Jan22

60% Plans Revising Schedule

Public Feedback 22Apr22

90% Plans Revising Schedule

Construction May23 - May24

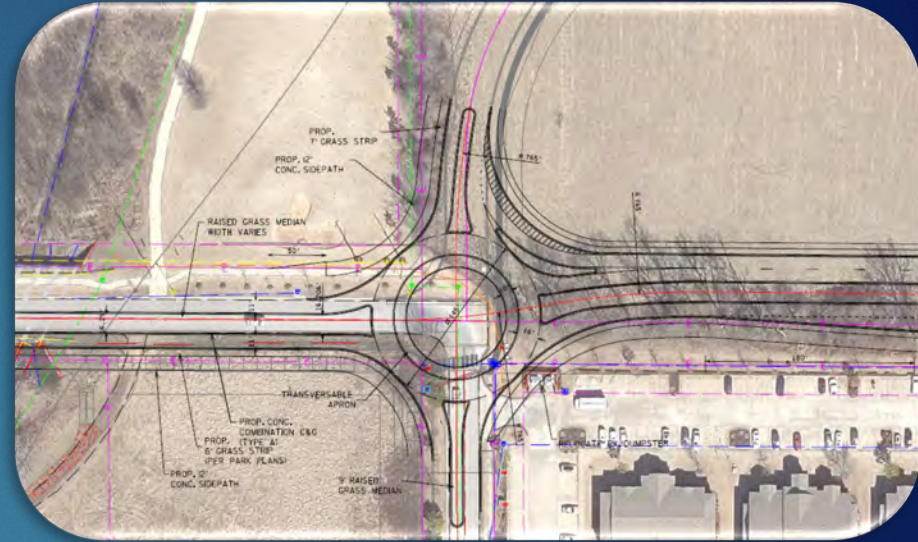

Notes

Project overview meeting with City staff Monday June 20.

Project Contacts

City of Bentonville: Andrea Jobe, PE
ajobe@bentonvillear.com

Engineer: Volkert: Reed Hill, P.E.
reed.hill@volkert.com

Contractor: TBD

Action Items

- Geotechnical evaluation by GHBW access.
- Review utilities with BEUD and Bentonville Water and Sewer.
- Revised cross section
- Redesign roadway for revised section
- Redesign drainage
- Revise project schedule
