

Tiger Blvd Overpass

Project Status Update 06MAY22

Project Schedule

Design Notice to Proceed: 19JUL21

30% Plan Submitted 28Jan22


Revised 30% Submitted 10Mar22

60% Plans 05May22

Public Feedback May22

90% Plans 23Sep22

Construction Jul23 - Sept24

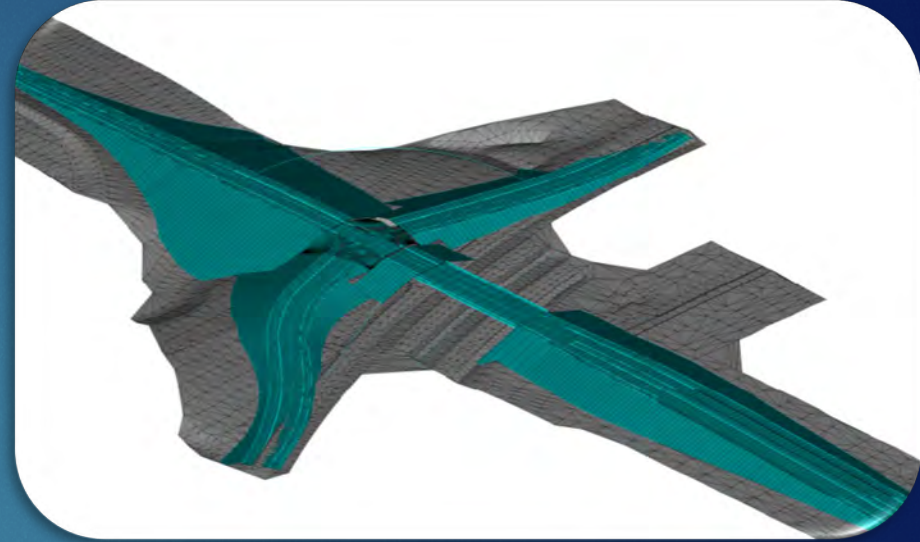

Notes

Updating survey and 60% plans to include underground BEUD.

Project Contacts

City of Bentonville: Jarrod Brightwell, PE
jbrightwell@bentonvillear.com

Engineer: Volkert - Ronny Loe, P.E.

Contractor: TBD ronny.loe@volkert.com

Action Items

- Review utility relocation plan from BEUD.
- Review utility relocation from Bentonville Water.
- Geotechnical evaluation by GHBW.
- Check on ARDOT Airspace permit progress.
