

# Tiger Blvd Overpass

Project Status Update 10MAR23

## Project Schedule

Design Notice to Proceed: 19JUL21


30% Plan Submitted 28Jan22

Revised 30% Submitted 10Mar22

60% Plans TBD

90% Plans TBD

Construction Sept23 - Nov24

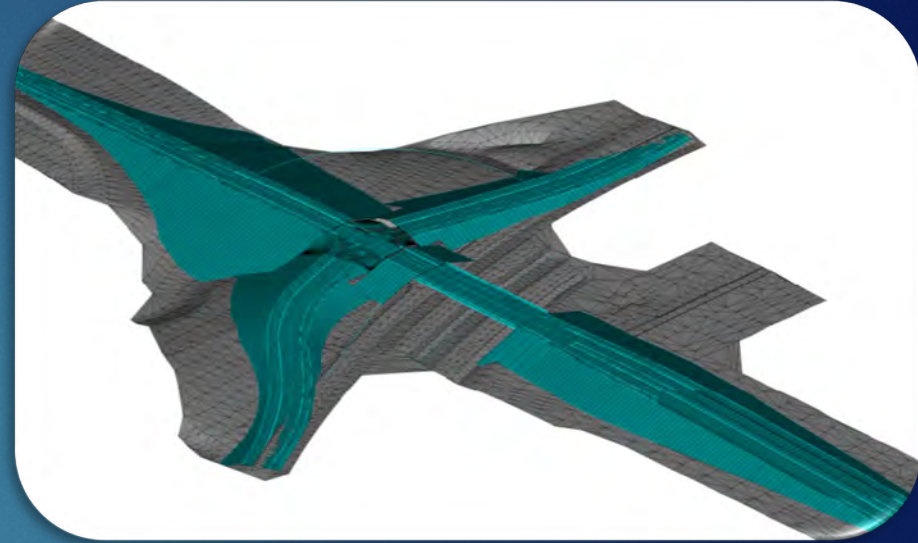

## Notes

Preparing ROW exhibits for discussion with property owners. Traffic and roundabout analysis complete.

## Project Contacts

City of Bentonville: Jarrod Brightwell, PE  
jbrightwell@bentonvillear.com

Engineer: Volkert - Ronny Loe, PE  
ronny.loe@volkert.com

Contractor: TBD

## Action Items

- Review utility relocation plan from BEUD.
- Review utility relocation from Bentonville Water.
- ARDOT Airspace permit in progress.
- BlackHills Energy review
