


# SW 14<sup>th</sup> & Been Intersection

Project Status Update 07SEP23

## Project Schedule

90% Plan Submittal: NOV23  
Final Plan Submittal: DEC23  
Project Bid: Reviewing Funding

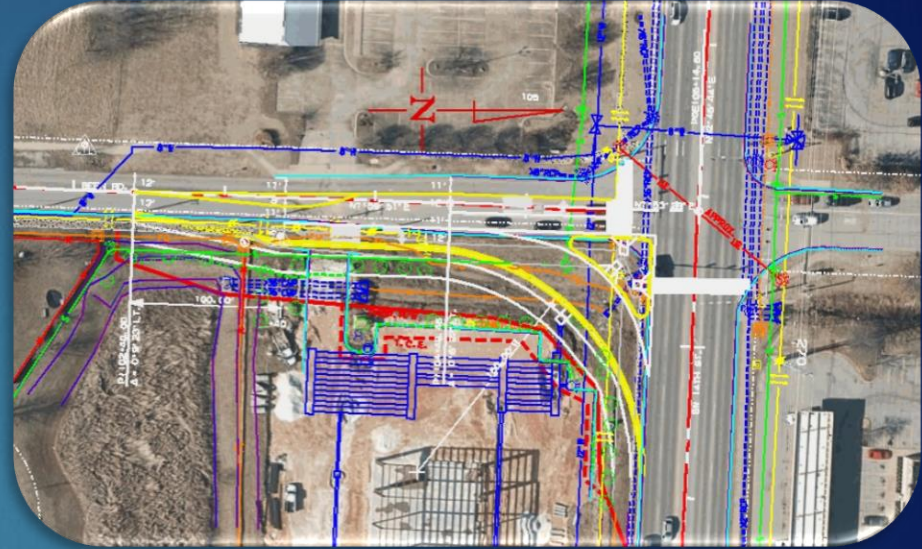

## Notes

60% Plans submitted 28JUL23

## Project Contacts

City of Bentonville: Cody Vaughn, EI  
cvaughn@bentonvillear.com  
Engineer: Jacobs Engineering Group  
Contractor: TBD

## Action Items

- Begin the pavement design.
- City to review 60% plans.
