


NW Trails End & C

Project Status Update 18 Nov22

Project Schedule

Design Notice to Proceed:
22JUL2021

Construction expected to begin spring/summer
2023, with completion expected fall 2023.

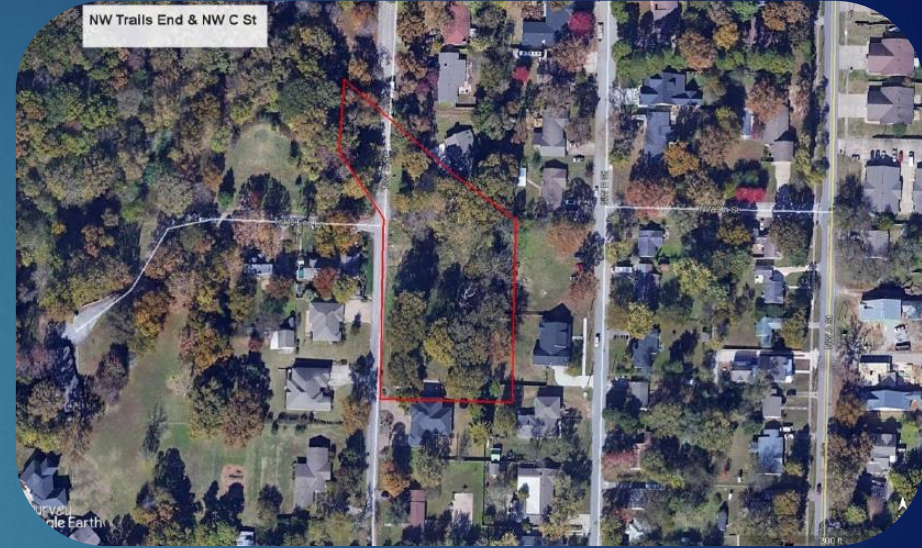

Notes

Revised 3rd submittal for final plans submitted to
eTrakit 11/17/22.

Project Contacts

City of Bentonville: Andrea Jobe, PE

ajobe@bentonvillear.com

Engineer: Aaron Boll, PE

Contractor: NA

Action Items

- ROW appraisal completed, contacting property owners
- Update plans to include sidewalk from development adjacent to project.
- Utility coordination
